

WEEKLY ADVANCE Weekly- 5 R0

PT. ORI POLYTEC COMPOSITES
 NAMA PROJECT : Kine - Supervisi
 PERIODE PROJECT : 18-24 September 2023
 NO SO : SOL230152

BUDGET USAGE :
 PROGRESS : 0.00%



NO.	DESCRIPTION	KETERANGAN				BUDGET		KETERANGAN
		PER	HARI	QTY	UNIT	HARGA (@)	JUMLAH	
1	MANPOWER COST							
	UANG MAKAN + SAKU (ENGINEERING)		7	1	hari	172,000	1,204,000	PER 18 - 24 SEPT 23
	SUB TOTAL-1						1,204,000	
2	MOBILISASI WORKER							
	Transport (AKOMODASI DI SITE)		1	1	minggu	300,000	300,000	
	SUB TOTAL-2						300,000	
3	AKOMODASI DI SITE							
	Penginapan		7	1	hr	Rp 400,000	2,800,000	
	SUB TOTAL-3						2,800,000	
4	CONSUMMABLES							
	Tools & Equipment					Rp -	-	
	SUB TOTAL-4						-	
5	LAIN-LAIN							
	biaya tak terduga						-	
	Pembulatan						-	
	SUB TOTAL-5						-	
	TOTAL						4,304,000	

NOTE :

Silahkan ditransfer ke rek. : 7285312167
 BANK : BCA
 an. Trisna

BUDGET	293,735,000	100.00%
REALISASI	26,686,267	9.09%
SISA BUDGET	267,048,733	90.91%
PROGRESS PEKERJAAN		


 Steven Chantano

Menyetujui
 Approved
 by
 WA
 Mansyur
 (Deputy Director)

08.55

4G 97%




Pak Mansyur



Panggilan suara tak terjawab pukul 14.02

Hari ini

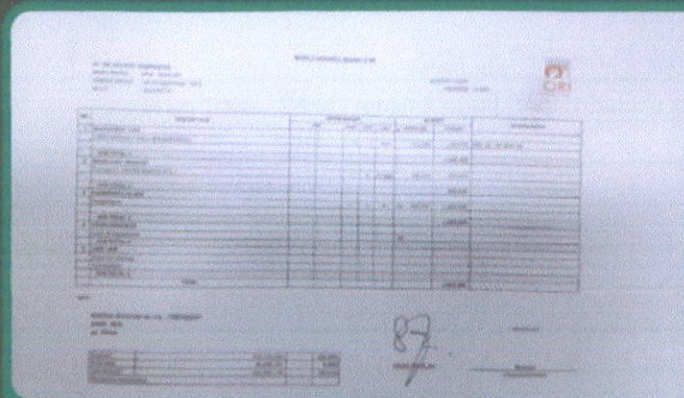

Dear Pak Mansyur, mohon dibantu approved pengajuan Adv weekly per 18-24 September 23, Project Lotte Supervisi, terlampir

08.12 ✓✓

1 pesan belum dibaca

ok

08.32



Ketik pesan



1

2

3

4

5

6

7

8

9

0

Q

W

E

R

T

Y

U

I

O

P

A

S

D

F

G

H

J

K

L



Z

X

C

V

B

N

M



!#1

,

Bahasa Indonesia

.





Doc No. : ENG-FSE-230067L-006

Rev : 0

DAILY FIELD SERVICE REPORT

Project : Line Project WP 4

Customer : Lotte E&C Indonesia

Contractor : KINE PROJECT JO

Contact Person : Mr. Eun Chul

General Activities W2**Saturday, 09 September 2023**

Barcol and visual check (1 spool Dn 800 and 1 spool Dn 1000) *Note : repair 1 spool (Defect bubble at internal).

Checking fit-up and inspection with DAEAH and KINE

Sunday, 10 September 2023

Continue monitoring lamination

Monday, 11 September 2023

Erection spool Dn 800 to piperack

Repairing defect spool

Check line and witness by DAEAH and KINE

Tuesday, 12 September 2023

Checking fit-up and approval for lamination (1 spool DN 1000 and 1 spool DN 800)

Thickness, bond length, barcol and visual check

Wednesday, 13 September 2023

Continue monitoring lamination DN 1000 and DN 800

Checking fit-up and inspection with DAEAH

Reported by : TRISNA RIZKY (Field Service Representative)

Acknowledged by : SURATNO (Supervisor KINE PROJECT JO)

Remarks :

DAILY FIELD SERVICE REPORT

Project : Line Project WP 4

Customer : Lotte E&C Indonesia

Contractor : KINE PROJECT JO

Contact Person : Mr. Eun Chul

Photo Activities



Fit-up spool elbow pipe DN 1000
09 September 2023



Monitoring lamination DN 1000
10 September 2023



Erection spool DN 800
11 September 2023



Bond Length DN 800
12 September 2023



Inspection with DAEAH
13 September 2023

Reported by : TRISNA RIZKY (Field Service Representative PT ORI POLYTEC COMPOSITES)

Acknowledged by : SURATNO (Supervisor KINE PROJECT JO)

Remarks :
